






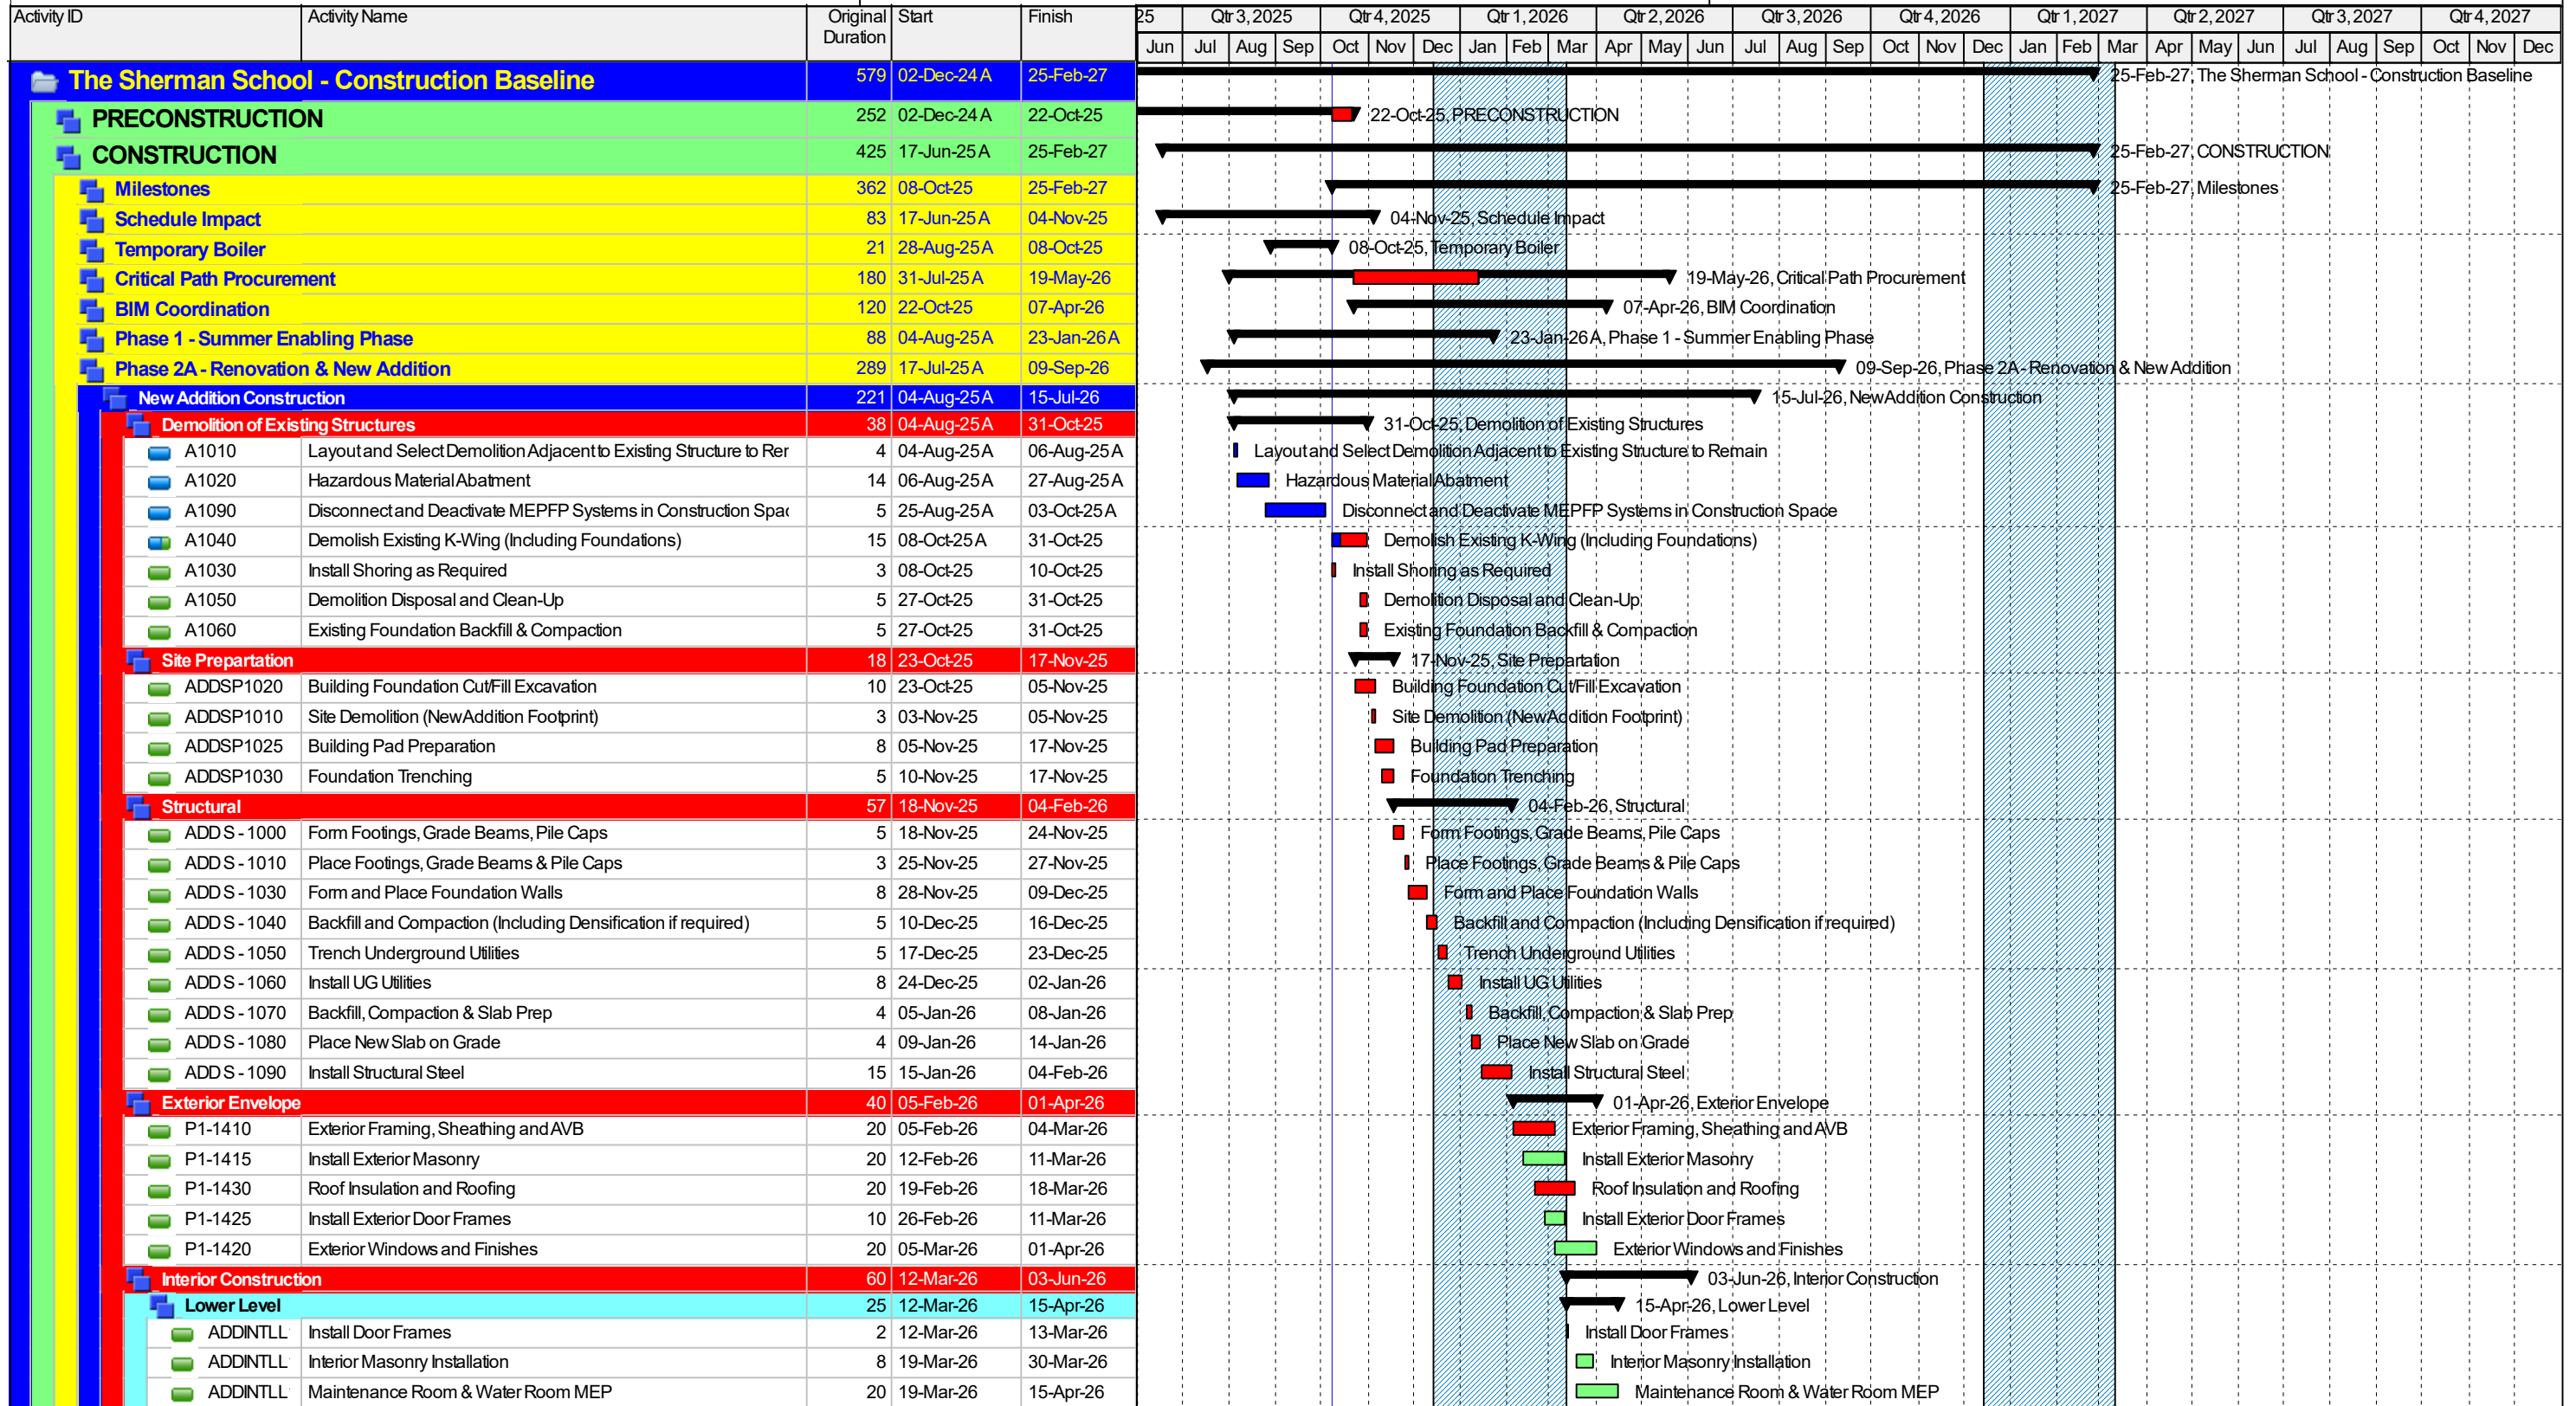

© Oracle Corporation

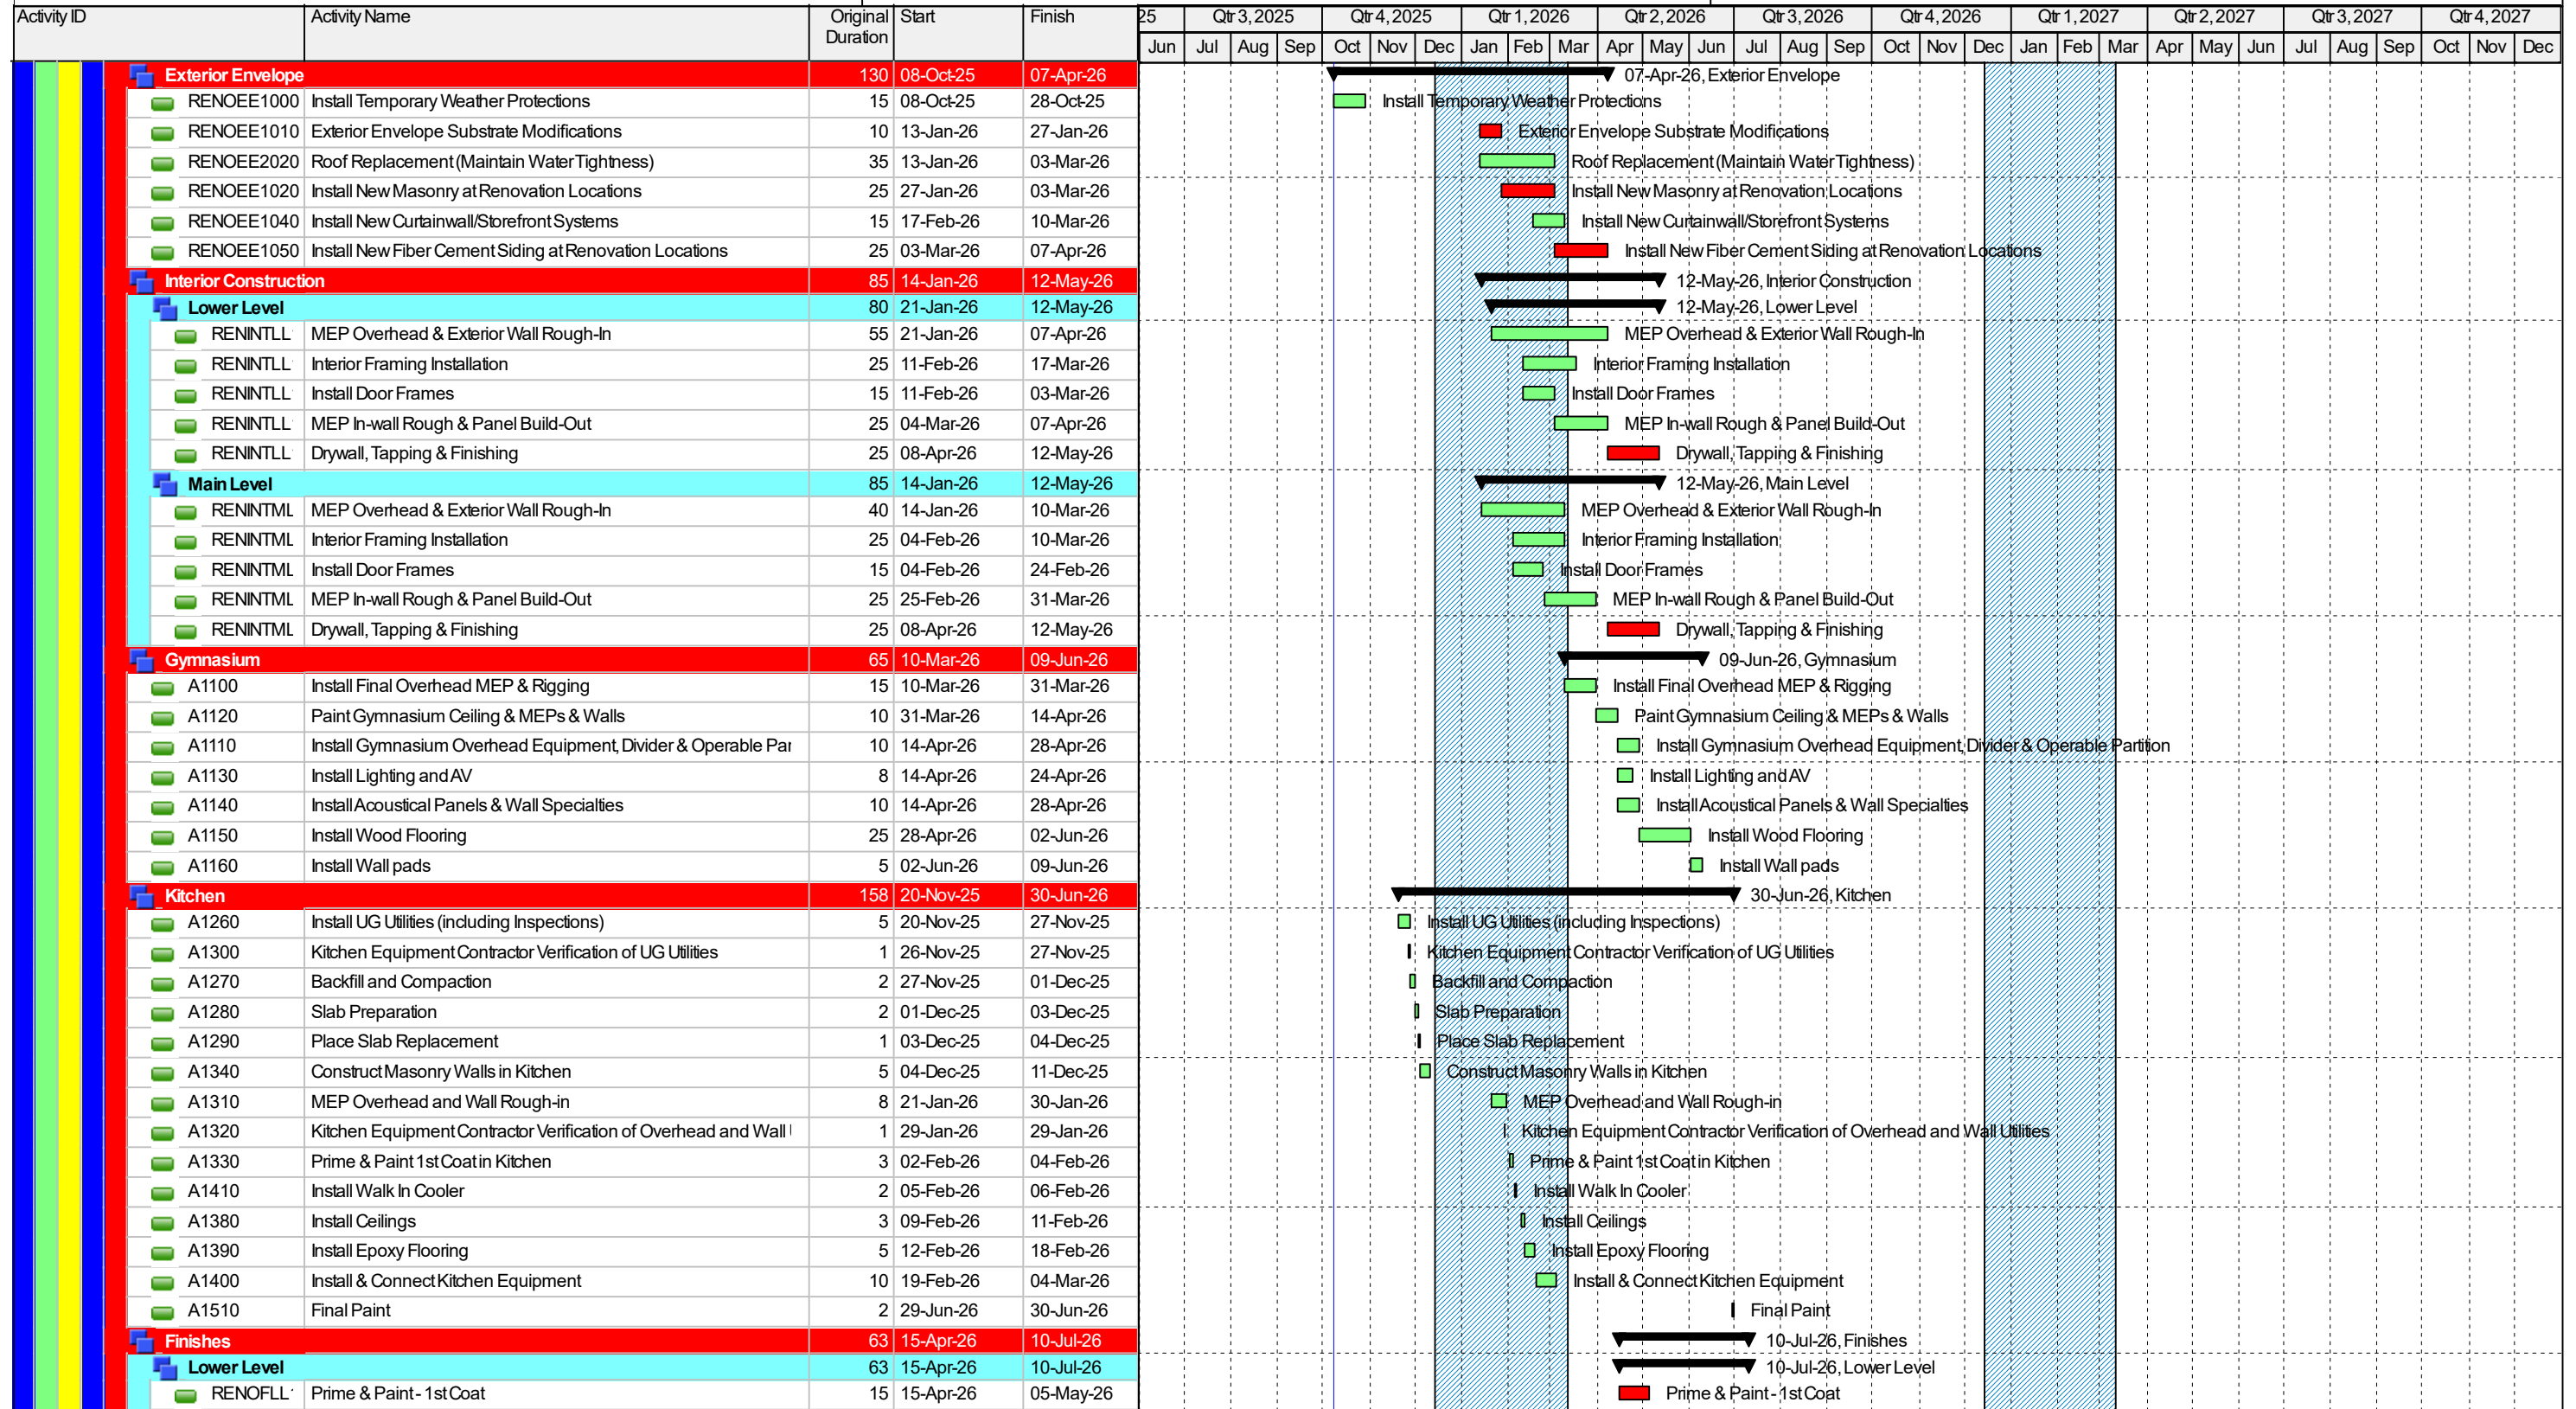

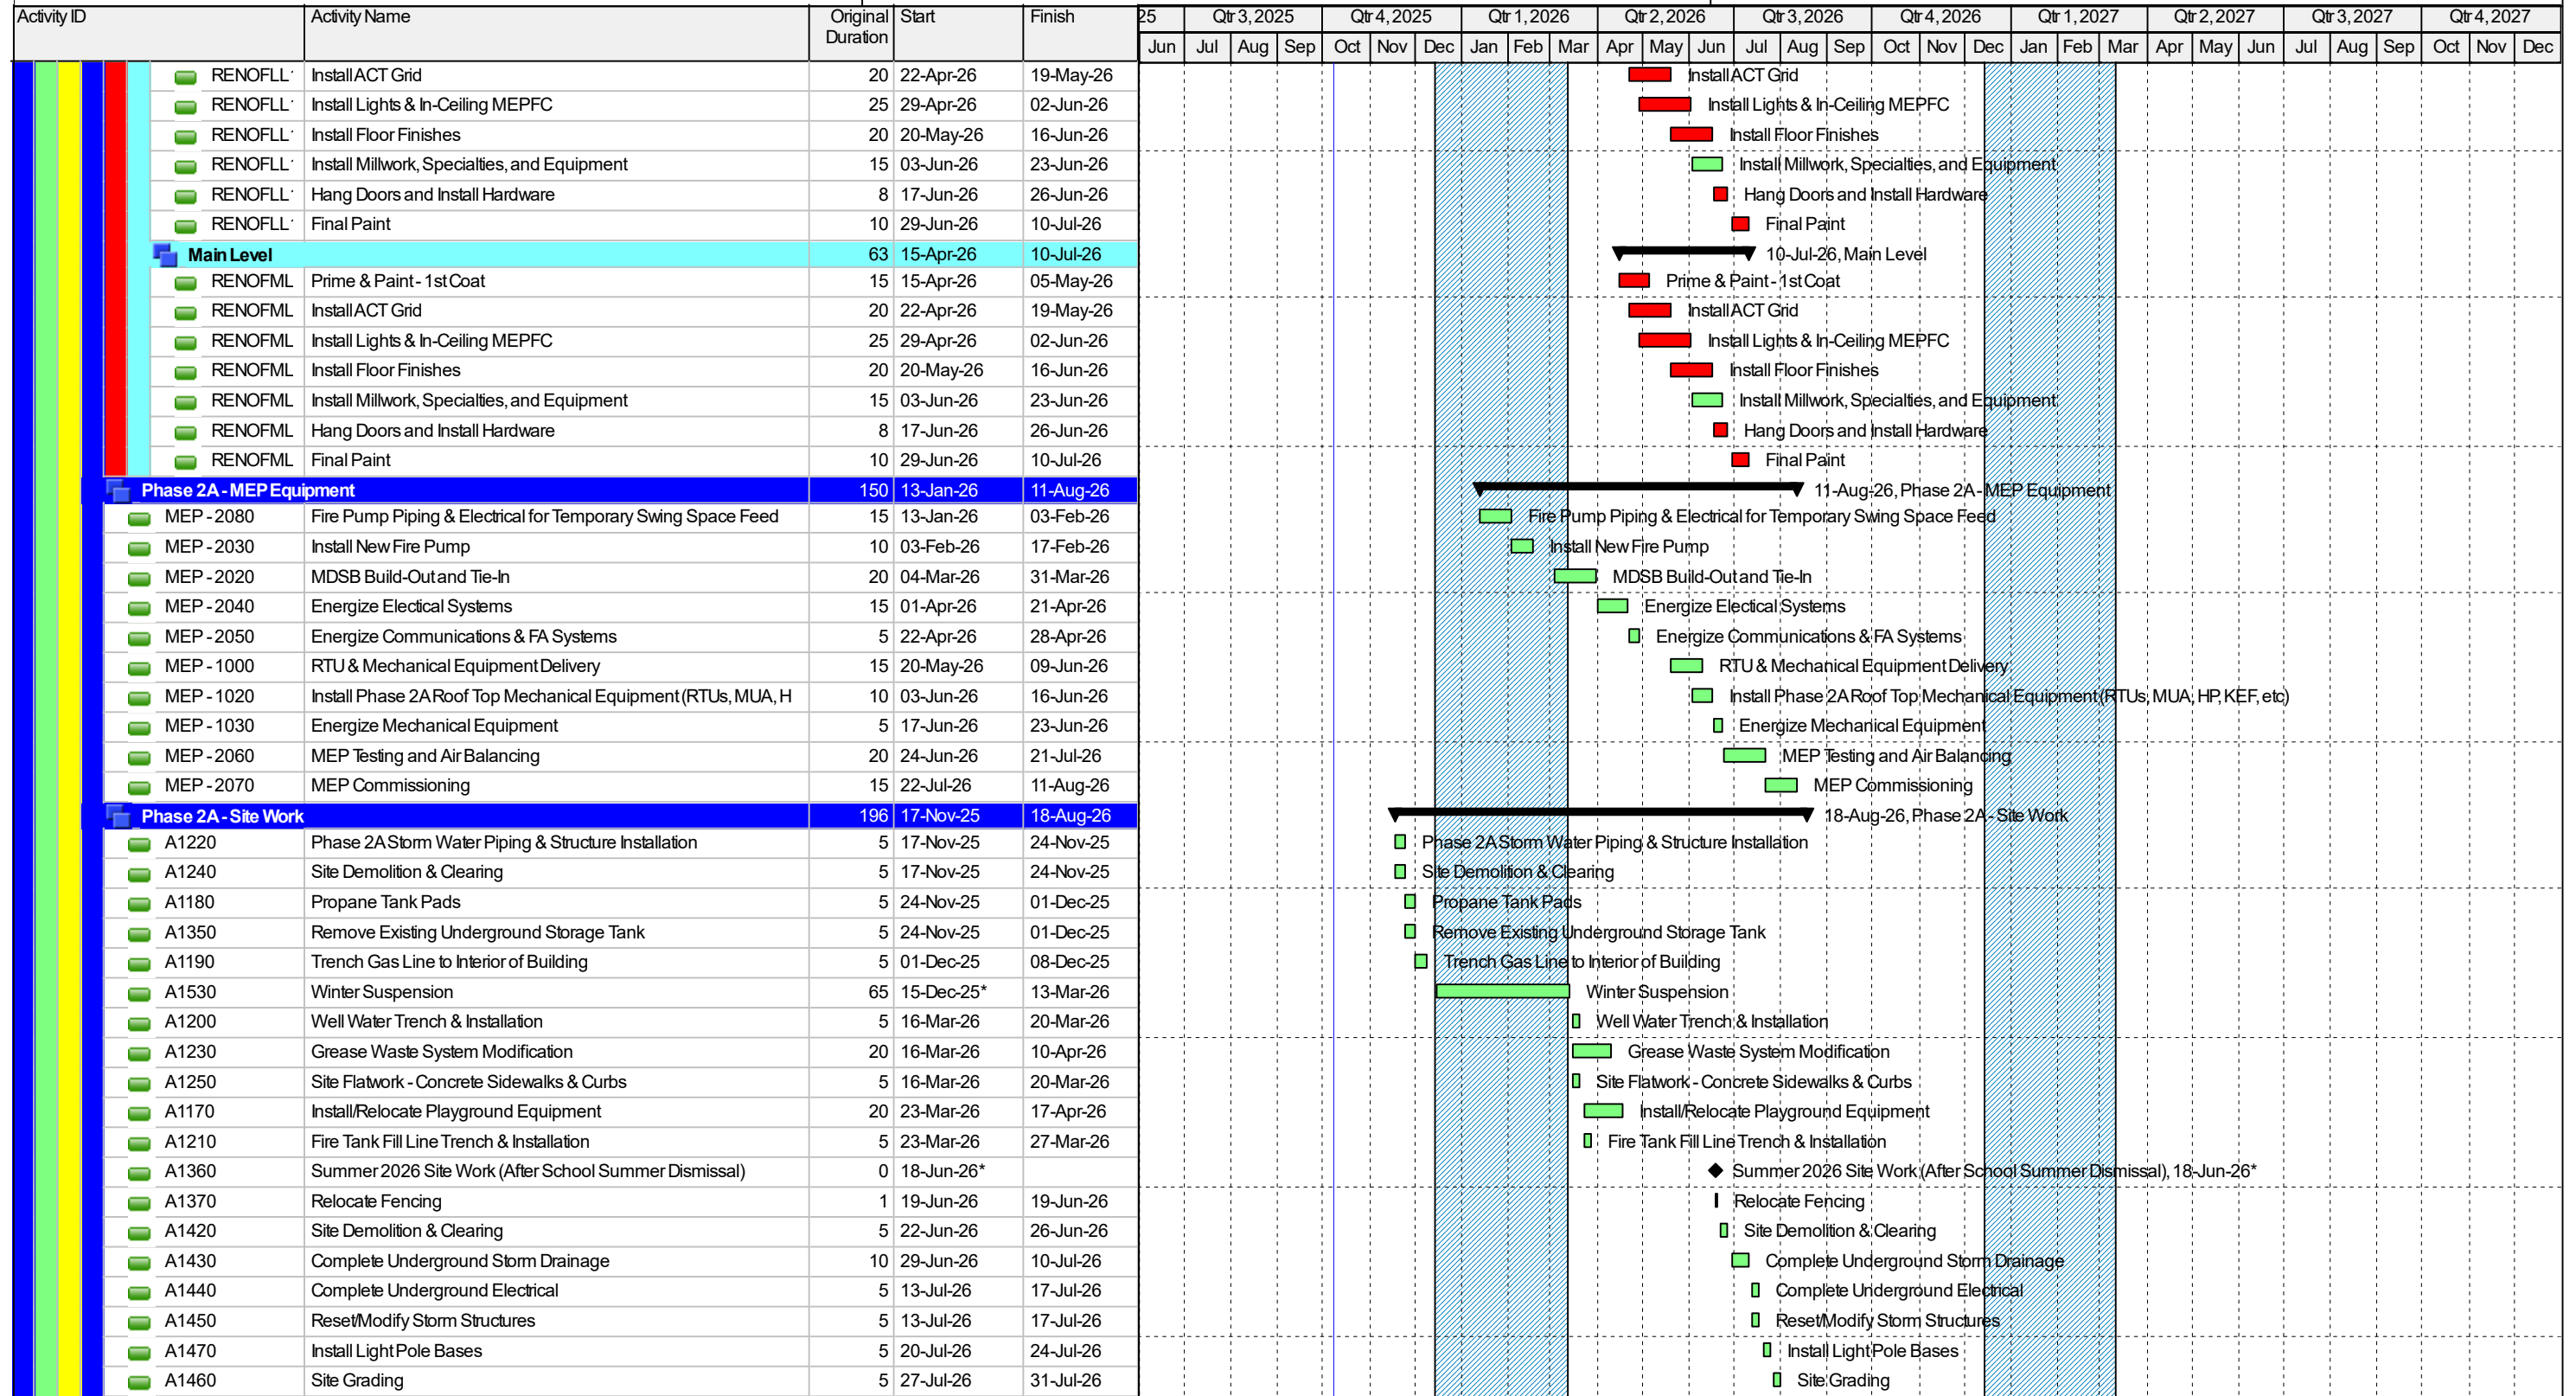

Activity ID		Activity Name	Original Duration	Start	Finish	25	Qtr 3, 2025				Qtr 4, 2025			Qtr 1, 2026			Qtr 2, 2026			Qtr 3, 2026			Qtr 4, 2026			Qtr 1, 2027			Qtr 2, 2027			Qtr 3, 2027			Qtr 4, 2027		
						Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	
A1490 A1480 A1500 Closeout F1000 F1010 F1030 F1040 F1110 F1120 Phase 2B - South Classroom Renovation Abatement & Select Demolition P2DEMO1000 P2DEMO1010 P2DEMO1050 P2DEMO1030 Site Preparation ADDSP1040 ADDSP1050 ADDSP1060 ADDSP1070 Structural ADDS - 1100 ADDS - 1110 ADDS - 1120 ADDS - 1190 ADDS - 1130 ADDS - 1140 ADDS - 1150 ADDS - 1160 ADDS - 1170 ADDS - 1180 Exterior Envelope P1-4050 P1-4060 P1-4080 P1-4090 P1-4070 Interior Construction ADDINTLL1100 ADDINTLL1110 ADDINTLL1120 ADDINTLL1130 ADDINTLL1140 Finishes RENOFLL1070	A1490	Fine Grading & Asphalt	5	03-Aug-26	07-Aug-26																																
	A1480	Landscapes	5	10-Aug-26	14-Aug-26																																
	A1500	Remove Site Fencing	2	17-Aug-26	18-Aug-26																																
	Closeout		40	16-Jul-26	09-Sep-26																																
	F1000	Initiate Punchlistand Final Clean	15	16-Jul-26	05-Aug-26																																
	F1010	Final Inspections	10	23-Jul-26	05-Aug-26																																
	F1030	Closeout Period	30	30-Jul-26	09-Sep-26																																
	F1040	Owner FF&E Move-In	20	30-Jul-26	26-Aug-26																																
	F1110	Teacher Occupancy	5	26-Aug-26	02-Sep-26																																
	F1120	First day of School Phase 2A Substantial Completion	0		02-Sep-26*																																
	Phase 2B - South Classroom Renovation		181	18-Jun-26	25-Feb-27																																
	Abatement & Select Demolition		19	18-Jun-26	14-Jul-26																																
	P2DEMO1000	Select Demolition For Abatement	4	18-Jun-26	23-Jun-26																																
	P2DEMO1010	D-Wing Abatment	5	24-Jun-26	30-Jun-26																																
	P2DEMO1050	Exterior Building Facade & Foundation Select Demolition	7	24-Jun-26	02-Jul-26																																
	P2DEMO1030	D-Wing Demolition (Including MEP Demo)	10	01-Jul-26	14-Jul-26																																
	Site Preparation		19	03-Jul-26	29-Jul-26																																
	ADDSP1040	Site Demolition (NewAddition Footprint)	5	03-Jul-26	09-Jul-26																																
	ADDSP1050	Building Foundation Cut/Fill Excavation	4	15-Jul-26	20-Jul-26																																
	ADDSP1060	BuildingArea Preparation	4	20-Jul-26	24-Jul-26																																
	ADDSP1070	Foundation Trenching	3	24-Jul-26	29-Jul-26																																
	Structural		40	30-Jul-26	23-Sep-26																																
	ADDS - 1100	Form Footings, Grade Beams, Pile Caps	4	30-Jul-26	04-Aug-26																																
	ADDS - 1110	Place Footings, Grade Beams & Pile Caps	3	05-Aug-26	07-Aug-26																																
	ADDS - 1120	Form and Place Foundation Walls	5	10-Aug-26	14-Aug-26																																
	ADDS - 1190	Form and Place Column Line B9 Footing & Frost Wall Extensions	3	10-Aug-26	12-Aug-26																																
	ADDS - 1130	Backfill and Compaction (Including Densification if required)	4	17-Aug-26	20-Aug-26																																
	ADDS - 1140	Trench Underground Utilities	5	21-Aug-26	27-Aug-26																																
	ADDS - 1150	Install UG Utilities	5	25-Aug-26	31-Aug-26																																
	ADDS - 1160	Backfill, Compaction & Slab Prep	6	27-Aug-26	03-Sep-26																																
	ADDS - 1170	Place New Slab on Grade	4	04-Sep-26	09-Sep-26																																
	ADDS - 1180	Install Structural Steel	10	10-Sep-26	23-Sep-26																																
	Exterior Envelope		23	24-Sep-26	26-Oct-26																																
	P1-4050	Exterior Framing, Sheathing and AVB	10	24-Sep-26	07-Oct-26																																
	P1-4060	Install Exterior Masonry	10	24-Sep-26	07-Oct-26																																
	P1-4080	Install Exterior Door Frames	2	28-Sep-26	29-Sep-26																																
	P1-4090	Roof Insulation and Roofing	18	01-Oct-26	26-Oct-26																																
	P1-4070	Exterior Windows and Finishes	10	08-Oct-26	21-Oct-26																																
	Interior Construction		25	27-Oct-26	30-Nov-26																																
	ADDINTLL1100	MEP Overhead & Exterior Wall Rough-In	20	27-Oct-26	23-Nov-26																																
ADDINTLL1110	Interior Framing Installation	10	03-Nov-26	16-Nov-26																																	
ADDINTLL1120	Install Door Frames	2	03-Nov-26	04-Nov-26																																	
ADDINTLL1130	MEP In-wall Rough & Panel Build-Out	10	10-Nov-26	23-Nov-26																																	
ADDINTLL1140	Drywall, Tapping & Finishing	15	10-Nov-26	30-Nov-26																																	
Finishes		26	01-Dec-26	05-Jan-27																																	
RENOFLL1070	Prime & Paint- 1st Coat	4	01-Dec-26	04-Dec-26																																	

 Actual Level of Effort  Remaining Work  Milestone
 Actual Work  Critical Remaining Work  summary



Town of Sherman
Sherman School District



Activity ID	Activity Name	Original Duration	Start	Finish	25	Qtr 3, 2025				Qtr 4, 2025			Qtr 1, 2026			Qtr 2, 2026		Qtr 3, 2026			Qtr 4, 2026			Qtr 1, 2027			Qtr 2, 2027			Qtr 3, 2027			Qtr 4, 2027		
					Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
	RENOFLL1080	Install ACT Grid	9	07-Dec-26	17-Dec-26																														
	RENOFLL1090	Install Lights & In-Ceiling MEPFC	5	09-Dec-26	15-Dec-26																														
	RENOFLL1100	Install Floor Finishes	4	11-Dec-26	16-Dec-26																														
	RENOFLL1120	Hang Doors and Install Hardware	2	21-Dec-26	22-Dec-26																														
	RENOFLL1110	Install Millwork, Specialties, and Equipment	8	21-Dec-26	30-Dec-26																														
	RENOFLL1130	Final Paint	4	31-Dec-26	05-Jan-27																														
	MEP Equipment		3	15-Dec-26	18-Dec-26																														
	A1070	Energize South Classroom MEPs	3	15-Dec-26	18-Dec-26																														
	Closeout		37	06-Jan-27	25-Feb-27																														
	F1050	Initiate Punchlist and Final Clean	8	06-Jan-27	15-Jan-27																														
	F1100	Commissioning & TAB	9	15-Jan-27	28-Jan-27																														
	F1060	Final Inspections	5	29-Jan-27	04-Feb-27																														
	F1070	Substantial Completion	0		04-Feb-27*																														
	F1080	Closeout Period	15	05-Feb-27	25-Feb-27																														
	F1090	Owner FF&E Move-In	15	05-Feb-27	25-Feb-27																														
	Phase 3 - Final Site Development & Landscaping		15	04-Feb-27	25-Feb-27																														
	A1080	Final Site Development & Landscaping	15	04-Feb-27	25-Feb-27*																														
	CLOSEOUT		15	05-Feb-27	25-Feb-27																														
	CLOSEOUT-1000	Closeout Documentation - Phase 2	15	05-Feb-27	25-Feb-27																														
	CLOSEOUT-1010	Final Completion	0		25-Feb-27																														
